



**PRIORITY PLANNING ADVISORY COMMITTEE
(PPAC)**

AGENDA

MEETING OF:

Wednesday, September 1, 2021



ADOT'S NONDISCRIMINATION NOTICE TO THE PUBLIC

The Arizona Department of Transportation (ADOT) hereby gives public notice that it is the Agency's policy to assure full compliance with Title VI of the Civil Rights Act of 1964, Title II of the Americans with Disabilities Act of 1990 (ADA), and other related authorities in all of its programs and activities.

ADOT's Title VI and ADA Programs require that no person shall, on the grounds of race, color, national origin, or disability, be excluded from participation in, be denied the benefits of, or be otherwise subjected to discrimination under any program or activity.

Any person, who believes his/her Title VI or ADA rights have been violated, may file a complaint. Any such complaint must be in writing and filed with the ADOT Civil Rights Office within one hundred eighty (180) days following the date of the alleged discriminatory occurrence. For additional information about ADOT's Civil Rights programs and the procedures to file a complaint contact ADOT Civil Rights Office via the information listed below:

AVISO PÚBLICO DE LA LEY DE NO-DISCRIMINACIÓN DE ADOT

El Departamento de Transporte del Estado de Arizona (ADOT) informa al público que esta agencia tiene como regla asegurar el cumplimiento total del Título VI de la Ley de los Derechos Civiles de 1964, del Título II de la Ley de ciudadanos Americanos con Discapacidades de 1990 (ADA) y otras normas relacionadas con todos sus programas y actividades.

Los programas del Título VI y ADA de ADOT exigen que a ninguna persona se le excluya de participar, se le nieguen beneficios o de ninguna otra manera sea sujeta a discriminación en ningún programa o actividad de ADOT por motivo de raza, color, país de origen, o discapacidad.

Cualquier persona que crea que se han violado sus derechos bajo el Título VI o el ADA, puede presentar una queja. Esta queja debe presentarse por escrito a la Oficina de Derechos Civiles de ADOT dentro de ciento ochenta (180) días a partir de la fecha en que se alega que ocurrió la discriminación. Para recibir más información sobre los programas de Derechos Civiles de ADOT y los procedimientos para presentar una queja, por favor póngase en contacto con la Oficina de Derechos Civiles de ADOT a través la información que aparece abajo:

FELICIA BELTRAN
TITLE VI NONDISCRIMINATION
PROGRAM COORDINATOR
FBELTRAN@AZDOT.GOV

KRYSTAL SMITH
ADA/NONDISCRIMINATION
PROGRAM COORDINATOR
KSMITH2@AZDOT.GOV

ADOT Civil Rights Office
206 S. 17th Avenue, Mail Drop 155-A
Phoenix, AZ 85007
602.712.8946
602.239.6257 FAX
azdot.gov

**ARIZONA DEPARTMENT OF TRANSPORTATION
MULTIMODAL PLANNING DIVISION
OFFICE MEMO**

TO: PRIORITY PLANNING ADVISORY COMMITTEE MEMBERS

DALLAS HAMMIT
KRISTINE WARD
STEVE BOSCHEN
BRENT CAIN
CLEMENC LIGOCKI
TIM LANE
BARRY CROCKETT
DON KRIZ
JON BRODSKY (Non Voting)

FROM: Chariman Gregory Byres

SUBJECT: PRIORITY PLANNING ADVISORY COMMITTEE MEETING (PPAC)

Pursuant to the A.R.S. 28-6951(B), the ADOT Director has appointed the members of the Priority Planning Advisory Committee (PPAC) to develop the Five Year Transportation Facilities Construction Program. This meeting is scheduled, pursuant to 28-6951(C4), to review the Program and make changes and schedule new projects into the adopted Five Year Transportation Facilities Construction Program.

Pursuant to Title VI of the Civil Rights Act of 1964, and the Americans with Disabilities Act (ADA), ADOT does not discriminate on the basis of race, color, national origin, age, sex or disability. Persons who require a reasonable accommodation based on language or disability should contact ADOT's Civil Rights Office at 602.712.8946 or at civilrightsoffice@azdot.gov. Requests should be made as early as possible to ensure the State has an opportunity to address the accommodation.


The meeting of the Arizona Department of Transportation, Priority Planning Advisory Committee (PPAC) will be held on Wednesday September 1, 2021 at 10:00AM. This will be held by teleconference. To access the meeting by the Internet, please go to meet.google.com/dhp-dpyu-err. To access the meeting by phone, please dial +1 540-835-0123, PIN 794 179 836#.

AGENDA:

1. Call to Order	Chairman
2. Roll Call	Information Only
3. Title VI the Civil Rights Act of 1964, as Amended	Information Only
4. Call to Audience	Information Only
5. Approval of the PPAC Minutes from 8/4/2021	Discussion and Possible Action Page 21
6. Program Monitoring Report	Information & Discussion

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-1 **Route & MP:** SR 377 @ MP 0.0
Project Name: SR 277 - SR 77
Type of Work: Road Safety Assessment (RSA)
County: Navajo
District: Northeast
Schedule:
Project: M718901X TIP#: 102763
Project Manager: Bahram Dariush
Program Amount: \$0
New Program Amount: \$140,000
Requested Action: Establish a new project.

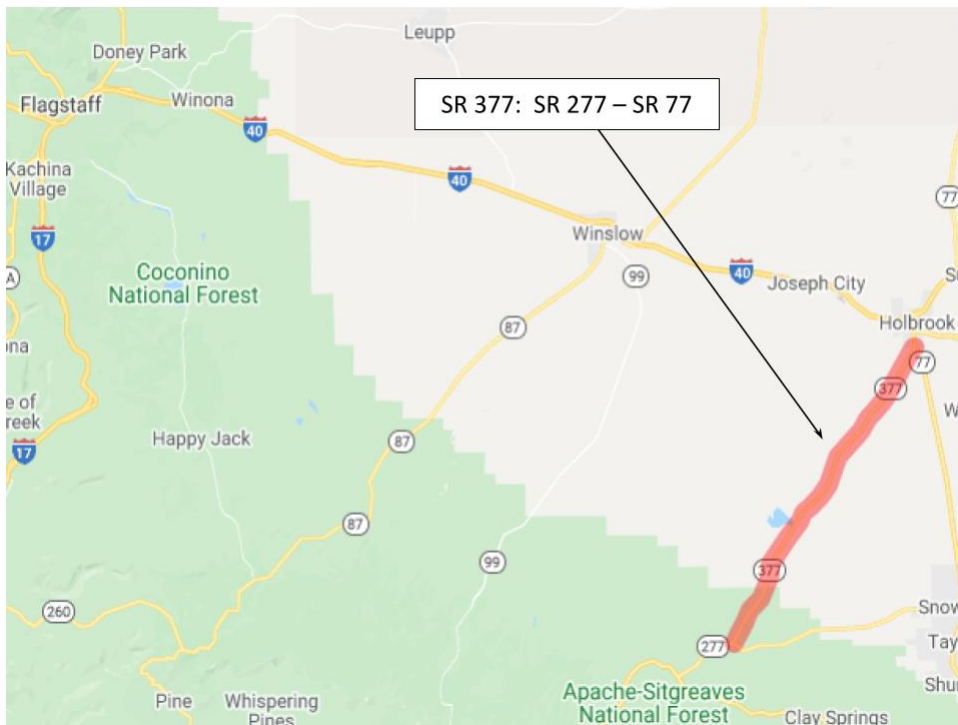

3. Form Date / 5. Form By:

8/25/2021

Bahram Dariush

4. Project Manager / Presenter:

Bahram Dariush @ 6027122332

1615 W Jackson St, 61, 065R - 6501 TRAFFIC HSIP

6. Project Name:

SR 277 - SR 77

7. Type of Work:

Road Safety Assessment (RSA)

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
-	Holbrook	377	Navajo	0.0	M718901X ?	33.8	377-A-NFA

16. Program Budget: \$0

17. Program Item #: 102763

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$140

18b Total Program Budget After Request:

\$140

CURRENTLY APPROVED:

19. BUDGET ITEMS:

CHANGE / REQUEST:

19A. BUDGET ITEMS:

Item #	Amount	Description	Comments
OTHR22	\$140	.	General Funds - FY 2020-2021 SB 1820

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

CHANGE REQUEST/NEW SCHEDULE:

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE:	NO	24f. MATERIALS MEMO COMP:	NO
24g. U&RR CLEARANCE:	NO	24h. C&S CLEARANCE:	NO
24i. R/W CLEARANCE:	NO	24j. CUSTOMIZED SCHEDULE:	NO
24k. SCOPING DOCUMENT:	NO		

25. DESCRIPTION OF REQUEST

Establish a new project.

26. JUSTIFICATION OF REQUEST

Senate Bill 1820 Section 33 has funding appropriations from the State General fund in fiscal year 2020-2021 to the Department of Transportation for highway projects. Part A of Section 33 lists highway projects to be funded. Item #21 listed, Study Guardrail - Shoulder of State Route 377 from Holbrook to Heber for the amount of \$140K. The RSA will perform a formal safety examination of the existing SR 377 and look at options to enhance safety.

27. CONCERNS OF REQUEST

28. OTHER ALTERNATIVES CONSIDERED

REQUESTED ACTIONS:

ESTABLISH A NEW PROJECT

APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
SUBJECT TO PPAC APPROVAL - 9/1/2021

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-2	Route & MP:	US 93 @ MP 193.0
	Project Name:	TEGNER ST - WICKENBURG RANCH WAY
	Type of Work:	CONSTRUCT DIVIDED HIGHWAY
	County:	Maricopa
	District:	Northwest
	Schedule:	
	Project:	F003101R TIP#: 8373
	Project Manager:	Craig Regulski
	Program Amount:	\$8,000,000
	New Program Amount:	\$11,000,000
	Requested Action:	Increase Right of Way sub-phase. Contingent upon MAG Regional Council approval.



3. Form Date / 5. Form By:

8/25/2021

Craig Regulski

4. Project Manager / Presenter:

Craig Regulski @ 6027128555

205 S 17th Ave, , E748 - 4983 PROJECT MANAGEMENT

6. Project Name:

TEGNER ST - WICKENBURG RANCH WAY

7. Type of Work:

CONSTRUCT DIVIDED HIGHWAY

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
AK10	Northwest	93	Maricopa	193.0	F003101R	5.0	NHPP093-B(215)S

16. Program Budget: \$8,000

17. Program Item #: 8373

18. Current Approved Program Budget:

\$8,000

18a. (+/-) Program Budget Request:

\$3,000

18b Total Program Budget After Request:

\$11,000

CURRENTLY APPROVED:

19. BUDGET ITEMS:

Item #	Amount	Description	Comments
8373	\$8,000	TEGNER ST - WICKENBURG RANCH WAY	

CHANGE / REQUEST:

19A. BUDGET ITEMS:

Item #	Amount	Description	Comments
71022	\$3,000	R/W ACQUISITION, APPRAISAL & PLANS	

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

CHANGE REQUEST NEW SCHEDULE:

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

PROJECT FUNDING VERIFIED BY PM

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE V

24e. ENVIRONMENTAL CLEARANCE:	YES	24f. MATERIALS MEMO COMP:	YES
24g. U&RR CLEARANCE:	NO	24h. C&S CLEARANCE:	NO
24i. R/W CLEARANCE:	NO	24j. CUSTOMIZED SCHEDULE:	YES
24k. SCOPING DOCUMENT:	YES		

25. DESCRIPTION OF REQUEST

Increase Right of Way sub-phase.

26. JUSTIFICATION OF REQUEST

Additional funding is required for the acquisition of parcels in condemnation due to recent increases in property values.

ICAP is included in this request.

27. CONCERNS OF REQUEST

28. OTHER ALTERNATIVES CONSIDERED

REQUESTED ACTIONS:

CHANGE IN BUDGET

APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
SUBJECT TO PPAC APPROVAL -
9/1/2021 Contingent on approval by MAG
Regional Council.

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-3	Route & MP:	Local Roads
	Project Name:	Harquahala Rd, Salome Rd to Monroe St
	Type of Work:	Roadway Lighting & Speed Feedback Signs
	County:	La Paz
	District:	Northwest
	Schedule:	
	Project:	T031601D TIP#: 100521
	Project Manager:	Dave Sabers
	Program Amount:	\$0
	New Program Amount:	\$30,000
	Requested Action:	Establish new project.



3. Form Date / 5. Form By:

8/19/2021

Dave Sabers

4. Project Manager / Presenter:

Dave Sabers @ (602) 712-7345

205 S. 17th Ave, MD 614 E - 4983 PROJECT MANAGEMENT

6. Project Name:

Harquahala Rd, Salome Rd to Monroe St

7. Type of Work:

Roadway Lighting & Speed Feedback Signs

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
RB1P	Northwest	0000	La Paz	LLA	T031601D ?	2.25	LLA-0(211)T

16. Program Budget: \$0

17. Program Item #: 100521

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$30

18b Total Program Budget After Request:

\$30

CURRENTLY APPROVED:

19. BUDGET ITEMS:

CHANGE / REQUEST:

19A. BUDGET ITEMS:

Item #	Amount	Description	Comments
70122	\$30	MODERNIZATION	PDA

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

CHANGE REQUESTNEW SCHEDULE:

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: IGA 21-0008185-1 **SIGNED:** YES **ADV:** YES

PROJECT FUNDING VERIFIED BY PM

CHANGE IN: **24a. PROJECT NAME:** NO **24b. TYPE OF WORK:** NO **24c. SCOPE:** NO **24d. CURRENT STAGE:** STAGE I

24e. ENVIRONMENTAL CLEARANCE:	NO	24f. MATERIALS MEMO COMP:	NOT APPLICABLE
24g. U&RR CLEARANCE:	NO	24h. C&S CLEARANCE:	NO
24i. R/W CLEARANCE:	NO	24j. CUSTOMIZED SCHEDULE:	NO
24k. SCOPING DOCUMENT:	NO		

25. DESCRIPTION OF REQUEST

Establish new project.

26. JUSTIFICATION OF REQUEST

This is a La Paz County 100pct HSIP funded project. The project will install roadway lighting and speed feedback signs along Harquahala Road. IGA was executed on June 8, 2021.

Staff \$30K

27. CONCERNS OF REQUEST

28. OTHER ALTERNATIVES CONSIDERED

REQUESTED ACTIONS:

ESTABLISH A NEW PROJECT

APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
 SUBJECT TO PPAC APPROVAL - 9/1/2021

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-4	Route & MP:	Local Roads
	Project Name:	Harquahala Rd, Salome Rd to Monroe St
	Type of Work:	Roadway Lighting & Speed Feedback Signs
	County:	La Paz
	District:	Northwest
	Schedule:	
	Project:	T031603D TIP#: 100521
	Project Manager:	Dave Sabers
	Program Amount:	\$0
	New Program Amount:	\$140,000
	Requested Action:	Establish new project.



3. Form Date / 5. Form By:
8/19/2021
Dave Sabers

4. Project Manager / Presenter:
Dave Sabers @ (602) 712-7345
205 S. 17th Ave, MD 614 E - 4983 PROJECT MANAGEMENT

6. Project Name:
Harquahala Rd, Salome Rd to Monroe St

7. Type of Work:
Roadway Lighting & Speed Feedback Signs

8. CPSID: RB1P 9. District: Northwest 10. Route: 0000 11. County: La Paz 12. Beg MP: LLA 13. TRACS #: T031603D ? 14. Len (Mi.): 2.25 15. Fed Id #: LLA-0(211)T

16. Program Budget: \$0 17. Program Item #: 100521

18. Current Approved Program Budget: \$0 18a. (+/-) Program Budget Request: \$140 18b Total Program Budget After Request: \$140

CURRENTLY APPROVED:

19. BUDGET ITEMS:

CHANGE / REQUEST:

19A. BUDGET ITEMS:

Table with 4 columns: Item #, Amount, Description, Comments. Row 1: 70122, \$140, MODERNIZATION, Consultant Design

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR:
22. CURRENT BID READY:
23. CURRENT ADV DATE:

CHANGE REQUEST/NEW SCHEDULE:

21A. REQUEST FISCAL YEAR:
22A. REQUEST BID READY:
23A. REQUEST ADV DATE:

20. JPA #'s: IGA 21-0008185-1 SIGNED: YES ADV: YES



CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE I

24e. ENVIRONMENTAL CLEARANCE: NO 24f. MATERIALS MEMO COMP: NOT APPLICABLE
24g. U&RR CLEARANCE: NO 24h. C&S CLEARANCE: NO
24i. R/W CLEARANCE: NO 24j. CUSTOMIZED SCHEDULE: NO
24k. SCOPING DOCUMENT: NO

25. DESCRIPTION OF REQUEST

Establish new project.

26. JUSTIFICATION OF REQUEST

This is a La Paz County 100pct HSIP funded project. The project will install roadway lighting and speed feedback signs along Harquahala Road. IGA was executed on June 8, 2021. Consultant Design. Consultant Design Fee was established by LA Paz County in request for HSIP funding. Any additional design costs will be the responsibility of the County.

Consultant \$140K

27. CONCERNS OF REQUEST

28. OTHER ALTERNATIVES CONSIDERED

REQUESTED ACTIONS:

ESTABLISH A NEW PROJECT


APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
SUBJECT TO PPAC APPROVAL - 9/1/2021

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-5 **Route & MP:** US 191 @ MP 154.0
Project Name: US 191 AT SR 75 & SR 78
Type of Work: CONSTRUCT ROUNDABOUT
County: Greenlee
District: Southeast
Schedule:
Project: F043801D TIP#: 102761
Project Manager: Jennifer Acuna
Program Amount: \$0
New Program Amount: \$600,000
Requested Action: Establish new design project.

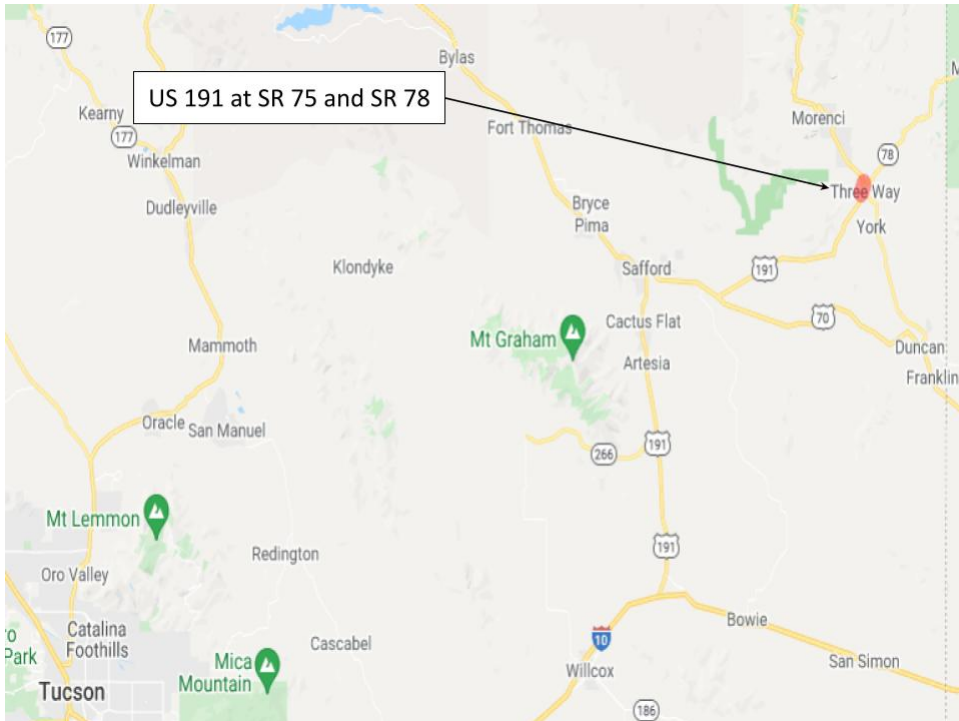

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-6	Route & MP:	Local Roads
	Project Name:	Hualapai Tribe – Diamond Bar Road
	Type of Work:	INSTALL RUMBLE STRIPS & SPEED FEEDBACK SIGNS
	County:	Mohave
	District:	Northwest
	Schedule:	
	Project:	_ TIP#: 100504
	Project Manager:	Mona Aglan-swick
	Program Amount:	\$0
	New Program Amount:	\$180,000
	Requested Action:	Establish a new project



3. Form Date / 5. Form By:

8/25/2021

Mona Aglan-swick

4. Project Manager / Presenter:

Mona Aglan-swick @ (602) 712-7374

1615 W Jackson St, 065R - 6501 TRAFFIC HSIP

6. Project Name:

Hualapai Tribe - Diamond Bar Road

7. Type of Work:

INSTALL RUMBLE STRIPS & SPEED FEEDBACK SIGNS

8. CPSID: 9. District: 10. Route: 11. County: 12. Beg MP: 13. TRACS #: 14. Len (Mi.): 15. Fed Id #:
- Kingman Mohave - ?

16. Program Budget: \$0 17. Program Item #: 100504

18. Current Approved Program Budget: \$0 18a. (+/-) Program Budget Request: \$180 18b Total Program Budget After Request: \$180

CURRENTLY APPROVED:

19. BUDGET ITEMS:

CHANGE / REQUEST:

19A. BUDGET ITEMS:

Table with 4 columns: Item #, Amount, Description, Comments. Row 1: 70122, \$180, MODERNIZATION

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

CHANGE REQUEST NEW SCHEDULE:

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: IGA 21-0008217-1 SIGNED: YES ADV: NO PROJECT FUNDING VERIFIED BY PM

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE: NO 24f. MATERIALS MEMO COMP: NO
24g. U&RR CLEARANCE: NO 24h. C&S CLEARANCE: NO
24i. R/W CLEARANCE: NO 24j. CUSTOMIZED SCHEDULE: NO
24k. SCOPING DOCUMENT: NO

25. DESCRIPTION OF REQUEST

Establish a new project

26. JUSTIFICATION OF REQUEST

The safety improvements on Diamond Bar Road include: Installation centerline and shoulder rumble strips over a 10 mile segment from MP 4.6 to Buck and Doe Road. Installation of four speed feed signs near the eastern and western project limits. The Hualapai Tribe experienced two fatal and two suspected incapacitating crashes within this roadway segment. A B/C ratio of 14.0 was calculated. This project is funded at 100pct HSIP federal funds and no local match. IGA was signed between ADOT, United States Department of the Interior BIA and Hualapai Indian Tribe in August 2021. HSIP funds will be transferred to BIA for Administration.

FY22 Design cost: \$180K

27. CONCERNS OF REQUEST

28. OTHER ALTERNATIVES CONSIDERED

REQUESTED ACTIONS:

ESTABLISH A NEW PROJECT

APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
SUBJECT TO PPAC APPROVAL - 9/1/2021

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-7	Route & MP:	SR 89A @ MP 387.0
	Project Name:	PUMPHOUSE WASH BRIDGE
	Type of Work:	CONSTRUCT BRIDGE REHABILITATION
	County:	Coconino
	District:	Northcentral
	Schedule:	FY 2022
	Project:	H877801C TIP#: 24215
	Project Manager:	Tricia Brown / Derek Boland
	Program Amount:	\$3,500,000
	New Program Amount:	\$5,700,000
	Requested Action:	Increase construction budget.



06

1. PRB Meeting Date: 8/24/2021 2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

8/25/2021

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown / Derek Boland @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

PUMPHOUSE WASH BRIDGE

7. Type of Work:

CONSTRUCT BRIDGE REHABILITATION

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
FQ1N	Northcentral	89A	Coconino	387.0	H877801C	1.0	STBGA89-B(217)T

16. Program Budget: \$3,500

17. Program Item #: 24215

18. Current Approved Program Budget:

\$3,500

18a. (+/-) Program Budget Request:

\$2,200

18b Total Program Budget After Request:

\$5,700

CURRENTLY APPROVED:**19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
24215	\$3,500	Pumphouse Wash Bridge	BRIDGE REPLACEMENT & REHABILITATION

CHANGE / REQUEST:**19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
76222	\$2,200	BRIDGE REPLACEMENT & REHABILITATION	

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR: 22
 22. CURRENT BID READY: 9/17/2021
 23. CURRENT ADV DATE: 10/22/2021

CHANGE REQUEST/NEW SCHEDULE:

21A. REQUEST FISCAL YEAR:
 22A. REQUEST BID READY:
 23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

CHANGE IN:	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	YES	24d. CURRENT STAGE:	STAGE V
-------------------	--------------------	----	--------------------	----	-------------	-----	---------------------	---------

24e. ENVIRONMENTAL CLEARANCE:	YES	24f. MATERIALS MEMO COMP:	YES
24g. U&RR CLEARANCE:	YES	24h. C&S CLEARANCE:	YES
24i. R/W CLEARANCE:	YES	24j. CUSTOMIZED SCHEDULE:	YES
24k. SCOPING DOCUMENT:	YES		

25. DESCRIPTION OF REQUEST

Increase construction budget.

26. JUSTIFICATION OF REQUEST

This project was originally advertised for construction on 10/22/2019. All bids were rejected. Restrictions and limitations placed on the contractor for maintenance of traffic activities were investigated during a Value Engineering (VE) study. The team proposed maintenance of traffic concepts that would provide more flexibility to the contractor and reduce costs. While the team identified some ways to reduce project costs, higher unit prices continue to increase construction costs.

This project will be advertised with H8907 Oak Creek Canyon for bundling efficiencies.

ICAP is included in this request.

27. CONCERNS OF REQUEST**28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN SCOPE
 CHANGE IN BUDGET


APPROVED / RECOMMENDED ACTIONS:

REQUEST APPROVED
 SUBJECT TO PPAC APPROVAL - 9/1/2021

PRB APPROVED

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-8	Route & MP:	SR 89A @ MP 388.0
	Project Name:	OAK CREEK CANYON
	Type of Work:	DRAINAGE AND SEDIMENT CONTROL
	County:	Coconino
	District:	Northcentral
	Schedule:	FY 2022
	Project:	H890701C TIP#: 6524
	Project Manager:	Tricia Brown / Derek Boland
	Program Amount:	\$2,300,000
	New Program Amount:	\$3,100,000
	Requested Action:	Increase construction budget.

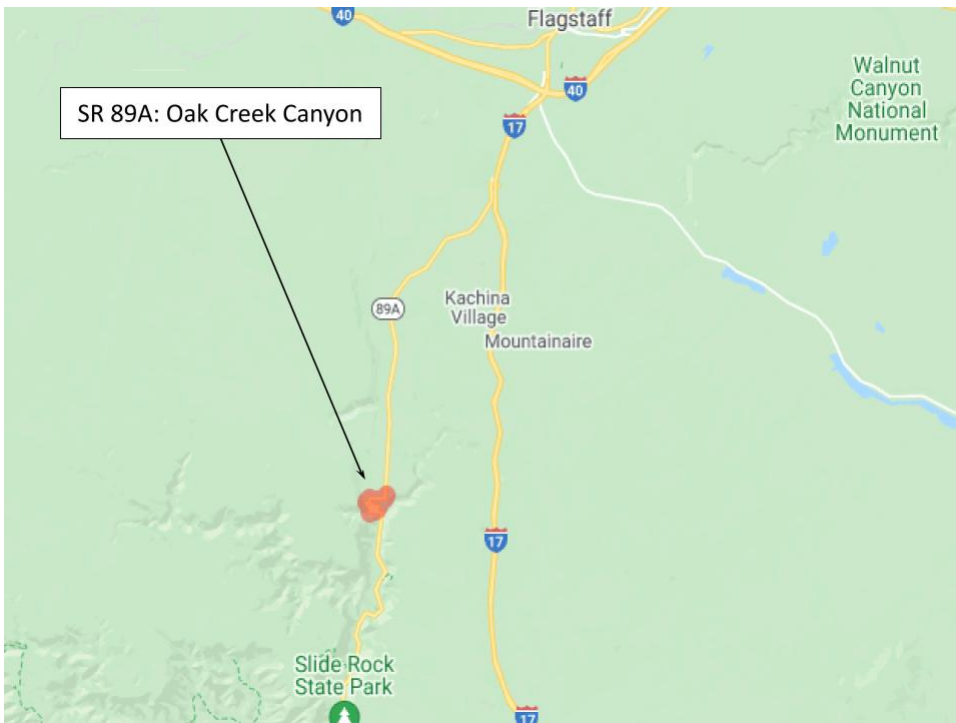

07

1. PRB Meeting Date: 8/24/2021 2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

8/25/2021

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown / Derek Boland @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

OAK CREEK CANYON

7. Type of Work:

DRAINAGE AND SEDIMENT CONTROL

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
NQ1N	Northcentral	89A	Coconino	388.0	H890701C	2.0	STP A89-B(218)T

16. Program Budget: \$2,300

17. Program Item #: 6524

18. Current Approved Program Budget:

\$2,300

18a. (+/-) Program Budget Request:

\$800

18b Total Program Budget After Request:

\$3,100

CURRENTLY APPROVED:**19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
OTHR20	\$498	.	.
6524	\$1,200	Oak Creek Canyon	REGULATORY COMPLIANCE
72320	\$602	CONTINGENCY	.

CHANGE / REQUEST:**19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72322	\$800	CONTINGENCY	.

CURRENT SCHEDULE:

21. CURRENT FISCAL YEAR: 22
 22. CURRENT BID READY: 9/17/2021
 23. CURRENT ADV DATE: 10/22/2021

CHANGE REQUESTNEW SCHEDULE:

21A. REQUEST FISCAL YEAR:
 22A. REQUEST BID READY:
 23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

 PROJECT FUNDING VERIFIED BY PM

CHANGE IN:	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	YES	24d. CURRENT STAGE:	STAGE V
-------------------	--------------------	----	--------------------	----	-------------	-----	---------------------	---------

24e. ENVIRONMENTAL CLEARANCE: YES

24f. MATERIALS MEMO COMP: YES

24g. U&RR CLEARANCE: YES

24h. C&S CLEARANCE: YES

24i. R/W CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

24k. SCOPING DOCUMENT: YES

25. DESCRIPTION OF REQUEST

Increase construction budget.

26. JUSTIFICATION OF REQUEST

This project was originally advertised for construction on 10/22/2019. All bids were rejected. The restrictions and limitations placed on the contractor for maintenance of traffic activities were investigated during a Value Engineering (VE) study. The team proposed maintenance of traffic concepts that would provide more flexibility to the contractor as well as a redesigned barrier footing to reduce costs. While the team identified some ways to reduce project costs, higher unit prices continue to increase construction costs.

This project will be advertised with H8778 Pumphouse Wash for bundling efficiencies.

ICAP is included in this request.

27. CONCERNS OF REQUEST**28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**CHANGE IN SCOPE
CHANGE IN BUDGET**APPROVED / RECOMMENDED ACTIONS:**REQUEST APPROVED
SUBJECT TO PPAC APPROVAL - 9/1/2021**PRB APPROVED**


7-9

AIRPORT PROGRAM:
GRANT MANAGER:

Tombstone Municipal Airport
Margie Cerda

REQUESTED ACTION:

The Sponsor is unable to meet the Grant agreement for proposed State/Local. Request is to cancel the project from the Statewide Airport Development Program.

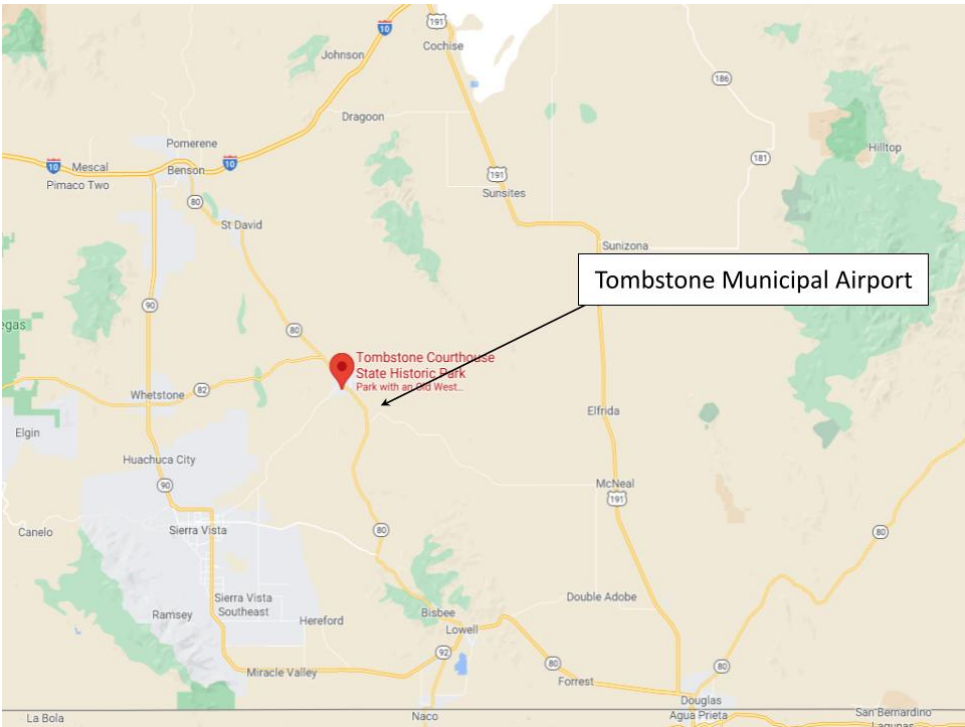


**ARIZONA DEPARTMENT OF TRANSPORTATION
MPD- Aeronautics Group**

Project Committee Recommendations

AIRPORT: TOMBSTONE MUNI New Project
SPONSOR: CITY OF TOMBSTONE Changed Project(s)
CATEGORY: Secondary
PROJECT NUMBER: E2S2D
GRANT MANAGER: MARGIE CERDA
AIP NUMBER: N/A (STATE LOCAL)
DATE: 8/11/21

Current Program Description	Fiscal Year	State Share	Sponsor Share	FAA Share	Total Amount	State Priority Number
MIRLs for Runway 6/24	22	\$76,000.00	\$4,000.00	N/A	\$80,000.00	216
Revised Program Description	Fiscal Year	State Share	Sponsor Share	FAA Share	Total Amount	State Priority Number
MIRLs for Runway 6/24	22	(\$76,000.00)	(\$4,000.00)	N/A	(\$80,000.00)	216
Recommended Action is:						
Sponsor is unable to meet Grant agreement for Proposed State Local. PPAC action is to cancel the project description to MIRLs for Runway 6/24. This Grant was in FY22 CIP, approved by STB 7/9/22.						

Aeronautics Recommends for PPAC action

Aeronautics Manager Approval:  **Date:** 8/11/2021
989A05EBCD984E2...
Don Kriz

FMS Review and Approval:  **Date:** 8/11/2021
2E9D65F44A19406...

8. Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held by teleconference until further notice. Time, date, and location may change and will be announced at the time of the distribution of the agenda.
- Information Only

- September 29, 2021 10:00am Wednesday
- November 3, 2021 10:00am Wednesday
- December 1, 2021 10:00am Wednesday

9. Adjourn Priority Planning Advisory Committee Meeting

WEB LINKS FOR REFERENCE

Priority Programming

http://www.azdot.gov/MPD/Priority_Programming/Index.asp

PPAC Meetings:

http://www.azdot.gov/MPD/Priority_Programming/PPAC/Index.asp

**DRAFT MINUTES FOR THE
ARIZONA DEPARTMENT OF TRANSPORTATION
PRIORITY PLANNING ADVISORY COMMITTEE
206 South 17th Avenue, Phoenix, AZ 85007
Teleconference Meeting
Wednesday August 4, 2021 @ 10:00AM**

The meeting of the Priority Planning Advisory Committee (PPAC) was held on Wednesday August 4, 2021 @ 10:00AM with Chairman Gregory Byres presiding.

Other committee members were present as follows:

Dallas Hammit, Steve Boschen, Clemenc Ligocki, Barry Crockett, Don Kriz, John Morales was the voting alternate for Tim Lane, and Elise Maza was the voting alternate for Kristine Ward.

1. CALL TO ORDER

Chairman Byres called the Priority Planning Advisory Committee meeting to order at 10:00AM.

2. ROLL CALL

Lynn Sugiyama conducted a roll call of the committee members. Brent Cain was unable to attend the meeting. A quorum was present.

3. TITLE VI OF THE CIVIL RIGHTS ACT OF 1964, AS AMENDED

Chairman Byres asked if any persons from the public were at the meeting. There were none. Chairman Byres stated that in accordance to the Title VI Civil Rights Act of 1964, and the Americans with Disabilities Act, ADOT will not discriminate on the basis of race, color, national origin, age, sex, or disability. If accommodations are requested, the public may contact someone on the PPAC Committee or the Civil Rights Office at 602-712-8964.

4. CALL TO THE AUDIENCE

Chairman Byres requested a call to the Audience for any comments or issues to be addressed, There were not comments from the audience.

5. APPROVAL OF PPAC MINUTES FROM THE 6/30/2021 MEETING

The minutes from the PPAC meeting held on 6/30/2021 were approved.

Chairman Byres called for a motion to approve the PPAC minutes from the meeting on 6/30/2021.

Steve Boschen made a motion to approve.

Don Kriz seconded the motion. The motion Motion carried unanimously.

6. PROGRAM MONITORING REPORT

The Program Monitoring Report was distributed to the Committee. Elise Maza stated that there were no comments on the report.

**7. 2022-2026 TRANSPORTATION FACILITIES CONSTRUCTION:
DISCUSSION AND POSSIBLE ACTION ON PROGRAM & PROJECT MODIFICATIONS**

7-1 **Route & MP:** I-10 @ MP 219.0
 Project Name: WYMOLA - INA RD
 Type of Work: County: INSTALL FIBER OPTICS
 District: Pinal
 Schedule: Southcentral
 Project: F043901D TIP#: 102706
 Project Manager: Jeffrey Davidson
 Program Amount: \$0
 New Program Amount: \$288,000
 Requested Action: Establish new project

**Chairman Byres called for a motion to approve Item 7-1.
 Steve Boschen made a motion to approve.
 Don Kriz seconded the motion. The motion carried unanimously.**

FY 2022-2026 Airport Development Program - Project Discussion and Possible Action

7-2 **AIRPORT PROGRAM:** State/Local Program (SL)
 GRANT MANAGER: Aeronautics Group - Greg Byres
 REQUESTED ACTION: The Aeronautics Group requests the SL Grants utilizing the Capital Outlay Appropriation in the amount of \$18 Million, be awarded to prioritized and eligible airports at a rate of 100 percent. The awarded grants would not require a match from the recipient airport.

**Chairman Byres called for a motion to approve Item 7-2.
 Steve Boschen made a motion to approve.
 Don Kriz seconded the motion. The motion carried unanimously.**

Discussion followed that a request to change the State Transportation Board Policy will be needed for Item 7-2 in order for it to be implemented. Item 7-2 will be revised. This will be given to the State Transportation Board for consideration on August 20th, 2021.

8. FUTURE MEETINGS

Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held in the ADOT Board Room, however, times, dates, and location may change and will be announced at the time of the distribution of the agenda.

September 1, 2021 on Wednesday at 10am.
September 29, 2021 on Wednesday at 10am.
November 3, 2021 on Wednesday at 10am.
December 1, 2021 on Wednesday at 10am.

9. ADJOURN PRIORITY PLANNING ADVISORY COMMITTEE MEETING

Chairman Byres called to adjourn the meeting.

Meeting adjourned at 10:08 am.

